

### JULY / AUGUST / SEPTEMBER



Facilities Management Department




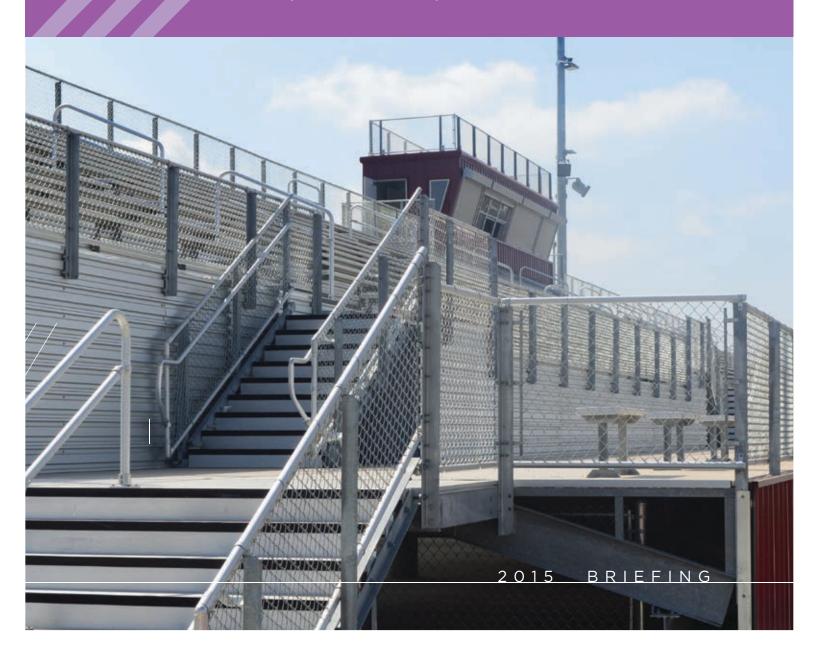

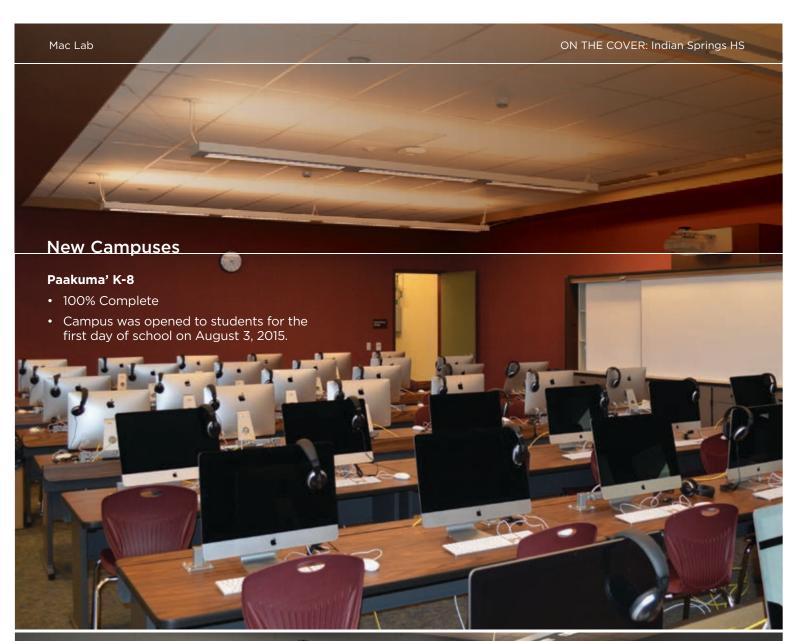

## **District-Wide Marquee Refurbishment and Replacement**


- Bids were opened and contract has been awarded for the refurbishment and replacement of school marquees at various locations.
  - 20 campuses are in the process of receiving new marquee signs.





#### **Dominguez Phase 2**

- 100% Complete
- Construction was completed and the Notice of Completion is pending.

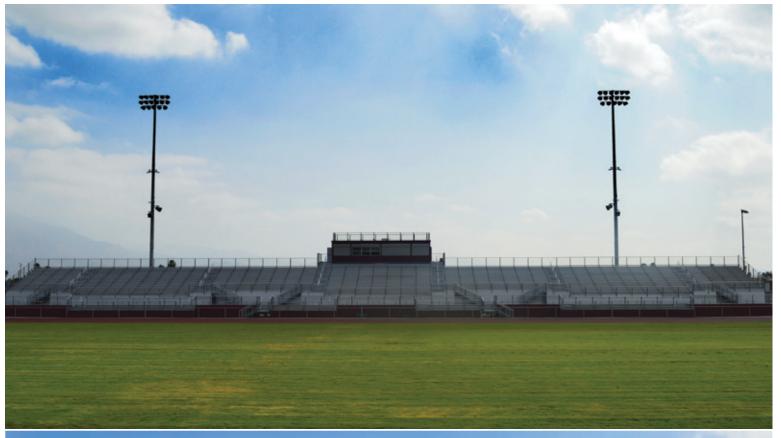





## Multiple ADA Upgrades at Various Elementary Schools

- 100% Complete
- Punch list items are all that remain prior to Notice of Completion.



## Multi-Purpose Building and CID Annex Remodel at the Community Day School

- 10% Complete
- Demolition is complete at CID Annex
- Above-ground demolition is complete at Multi-Purpose Building
- Installation of fire sprinklers, duct work and electrical conduits is underway

#### **Professional Development Center**

- 10% Complete
- Installation of new data network cabling is underway.
- Interior design layout is complete.
- Parking lot construction is anticipated to begin in the fourth quarter of 2015.



#### **Riley ES and Richardson PREP Lunch Shelters**

- Construction contract was awarded in August of 2015.
- Structures have been ordered and fabrication is in process.



#### **Security and Surveillance Systems**

 Installation of new security and surveillance systems includes new cameras and infrastructures that report to the School Police Department. Systems have been installed at the Board of Education, Community Day School (CDS), Maintenance and Operations, Professional Development Center, SMART Building and the WHAA Building as well as at the following schools:

Arroyo Valley HS Middle College HS Brown ES Norton ES Cajon HS Paakuma' K-8 Pacific HS Cole ES Curtis MS Riley ES Cypress ES Roberts ES Del Rosa ES Roosevelt ES Dominguez ES San Andreas HS

Henry ES Sierra HS

Hunt ES San Gorgonio HS
Indian Springs HS Thompson ES
Kimbark ES Warm Springs ES
Lankershim ES Wilson ES

San Bernardino HS

Lincoln ES Wilson ES

Lincoln ES Wong ES

 Installation of new systems is planned for Chavez, Del Vallejo, Martin Luther King, Richardson, Serrano, Shandin Hills Middle Schools.

#### **SMART Building Upgrades**

• 99% Complete

Gomez ES

- Original contract scope is now complete.
- Additional, unforeseen scope that is required to complete the project, will begin fourth quarter 2015.

## Overcrowding Relief Grant (ORG) and Special Day Classroom (SDC) Projects

#### Lytle Creek Elementary School ORG and SDC

- 100% Complete
- Punch list items are all that remain prior to Notice of Completion



#### **Upcoming Projects:**

#### **Cajon High School Little Theatre Renovation**

- First design phase has been reviewed by the Division of State Architect (DSA).
- Soils report testing is now complete.
- · Continued design is ongoing.
- Submission to DSA is anticipated for the fourth quarter of 2015.

#### **Indian Springs High School Performing Arts Center**

- Architect selection and preliminary design are now complete.
- Submission to DSA is anticipated for the first quarter of 2016.

#### **San Bernardino High School Auditorium Renovation**

• Design plans have been submitted to the Division of State Architect (DSA).

#### **Track Improvements**

 Architect selection is underway for Track Improvements at Arroyo Valley HS, Cajon HS, Pacific HS and San Bernardino HS.



# <u>Cajon High School</u>

#### **Anticipated Construction Projects Schedules**

#### **New Campuses**

	20	13			20	14		2015				2016			
Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4
											Paal	kumá	K-8		

PROJECTS IN CONSTRUCTION

#### **Overcrowding Relief Grant (ORG) Projects**


	20	13			20	14			20	15		2016			
Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4
								Lytle Creek ES							
					Wilson ES										
PROJECTS IN CONSTRUCTION COMPLETED PROJECTS															

#### **Other Projects**

	20	13		2014					20	15		2016			
Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4
	Dominguez ES Phase 2														
	Indian Springs HS Athletic Complex														
Multiple ADA Upgrades															
					MPR 8	k Anne	x Rem	odel @	CDS						
		Prof	ession	al Dev	elopm	ent Ce	nter								
	Smart Building Upgrades														
					Securit	y Upg	rades								

PROJECTS IN CONSTRUCTION

#### **Upcoming Projects**



ANTICIPATED CONSTRUCTION

#### **The Board of Education**

Mr. Michael J. Gallo, President

Mrs. Margaret Hill, Vice President

Dr. Barbara Flores

Mrs. Abigail Medina

Mrs. Gwendolyn Rogers

Mrs. Lynda K. Savage

Mr. Danny Tillman

#### Superintendent

Dr. Dale Marsden

#### District Facilities, M&O Administrators

John Peukert

**Assistant Superintendent** 

Samer Alzubaidi

**Facilities Director** 

**Ed Norton** 

Maintenance & Operations Director

## Facilities Program Management Team

AECOM

Rafael Quezon, Program Manager



Written and published by: Facilities Management Department September 2015
