

APRIL / MAY / JUNE









Dominguez Phase 2

- 70% Complete
- Construction bids were opened on April 23, 2015
- Construction began on June 11, 2015 with the installation of classroom tackwall.

Multiple ADA Upgrades at Various Elementary Schools

- Construction began on June 1, 2015.
- Demolition and concrete installation are now complete at Barton ES.
- Path of Travel upgrades are now complete at Rio Vista ES.
- Ramp construction is near completion at Highland Pacific ES.
- Demolition is underway at Cypress and Emmerton ES.







Indian Springs HS - Athletic Complex



- 50% Complete
- New bleachers, press box and field lighting now installed

Indian Springs High School Athletic Complex

 Swimming pool concrete slab and walls have been poured.

Pacific High School ADA Upgrades


- 100% Complete
- Punch list work is complete.
- Contractors are off campus.

Professional Development Center

- Property purchased on December 30, 2014.
- Flooring demolition on the first floor is now complete.
- Installation of surveillance system and network equipment is complete.
- Design for the parking lot addition is underway





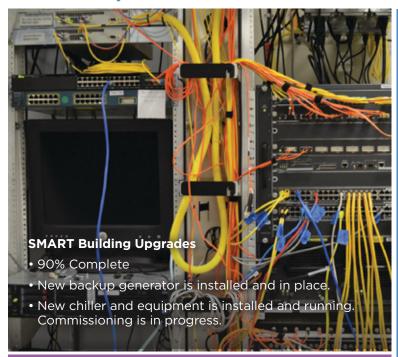

Security Replacement/Upgrades

- Security system installations are now complete.
- Punch list work is all that remains.

Security and Surveillance Systems

• Installation of new security and surveillance systems includes new cameras and infrastructures that report to the School Police Department. Systems have been installed at the Board of Education, Community Day School (CDS), Professional Development Center, SMART Building and the WHAA Building as well as at the following schools:

Arroyo Valley HS Middle College HS **Brown ES** Norton ES Cajon HS Paakuma' K-8 Cole ES Pacific HS Curtis MS Riley ES Cypress ES Roberts ES Roosevelt ES Del Rosa ES Dominguez ES San Andreas HS Gomez ES San Bernardino HS

Henry ES Sierra HS

Hunt ESSan Gorgonio HSIndian Springs HSThompson ESKimbark ESWarm Springs ES

Lankershim ES Wilson ES
Lincoln ES Wong ES

 Installation of new systems is planned for Muscoy ES, Maintenance and Operations and Nutrition Services.



Overcrowding Relief Grant (ORG) and Special Day Classroom (SDC) Projects

Lytle Creek Elementary School ORG and SDC

- 90% Complete
- Installation of finishes including flooring, plumbing fixtures, restroom tile and partitions is ongoing.
- Site concrete, asphalt, and fencing is underway.

Wilson Elementary School ORG and SDC

- 100% Complete
- Construction is now complete and teachers have moved from portable classrooms into new permanent classrooms.



San Bernardino HS - Auditorium Rendering

Upcoming Projects:

Cajon High School Little Theatre Renovation

- Architect selection is complete and the renovation is in the programming phase.
- Survey and soils testing are ongoing.

Indian Springs High School Performing Arts Center

• Architect selection is ongoing with Board approval anticipated in the third quarter of 2015.

Multi-Purpose Room and CID Annex Remodel at the Community Day School

- Construction bids were opened on June 17, 2015
- Notice to Proceed will be issued upon Contractor Board Approval, anticipated in July 2015.

Riley ES and Richardson PREP Lunch Shelters

- Plans for the construction and installation of lunch shelters were approved by the Division of State Architect (DSA) in May 2015.
- Construction bids were opened on June 2, 2015 and Contractor Board Approval is anticipated in July 2015.

San Bernardino High School Auditorium Renovation

• Development of plans is ongoing.

San Bernardino

Anticipated Construction Projects Schedules

New Campuses

2013					20	14			20	15					
Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4
		Paakumá K-8													

PROJECTS IN CONSTRUCTION

Overcrowding Relief Grant (ORG) Projects

	20	13			20	14		2015					2016			
Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	
				Lytle Creek ES												
				Wilson ES												
PF	PROJECTS IN CONSTRUCTION COMPLETED PROJECTS															

Other Projects

	20	13			20	14			20	15					
Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4
	Dominguez ES Phase 2														
	Indian Springs HS Athletic Complex														
					Multip	le ADA	\ Upgr	ades							
	Professional Development Center														
	Smart Building Upgrades														
					Securit	y Upg	rades								

PROJECTS IN CONSTRUCTION

Upcoming Projects

	20	13			20	14			20	15			20	16	
Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4
San Bernardino HS Auditorium Renovation															
				Cajon HS Theatre Renovation											
								India	n Spri	ngs HS	Perfo	rming	Arts C	enter	
MPR & Annex Remodel @ CDS															
		1	Riley E	S, Ricl	hardso	n PREI	P - Lun	ch She	elters						

ANTICIPATED CONSTRUCTION

The Board of Education

Mr. Michael J. Gallo, President

Vacant, Vice President

Dr. Barbara Flores

Mrs. Margaret Hill

Mrs. Abigail Medina

Mrs. Lynda K. Savage

Mr. Danny Tillman

Superintendent

Dr. Dale Marsden

District Facilities, M&O Administrators

John Peukert

Assistant Superintendent

Samer Alzubaidi

Facilities Director

Ed Norton

Maintenance & Operations Director

Facilities Program Management Team

AECOM

Steve Massetti, Program Manager



Written and published by: Facilities Management Department July 2015
